


Day & Night Work: Victoria Park Avenue to Main Street

Construction Update - April 2022 to May 2023

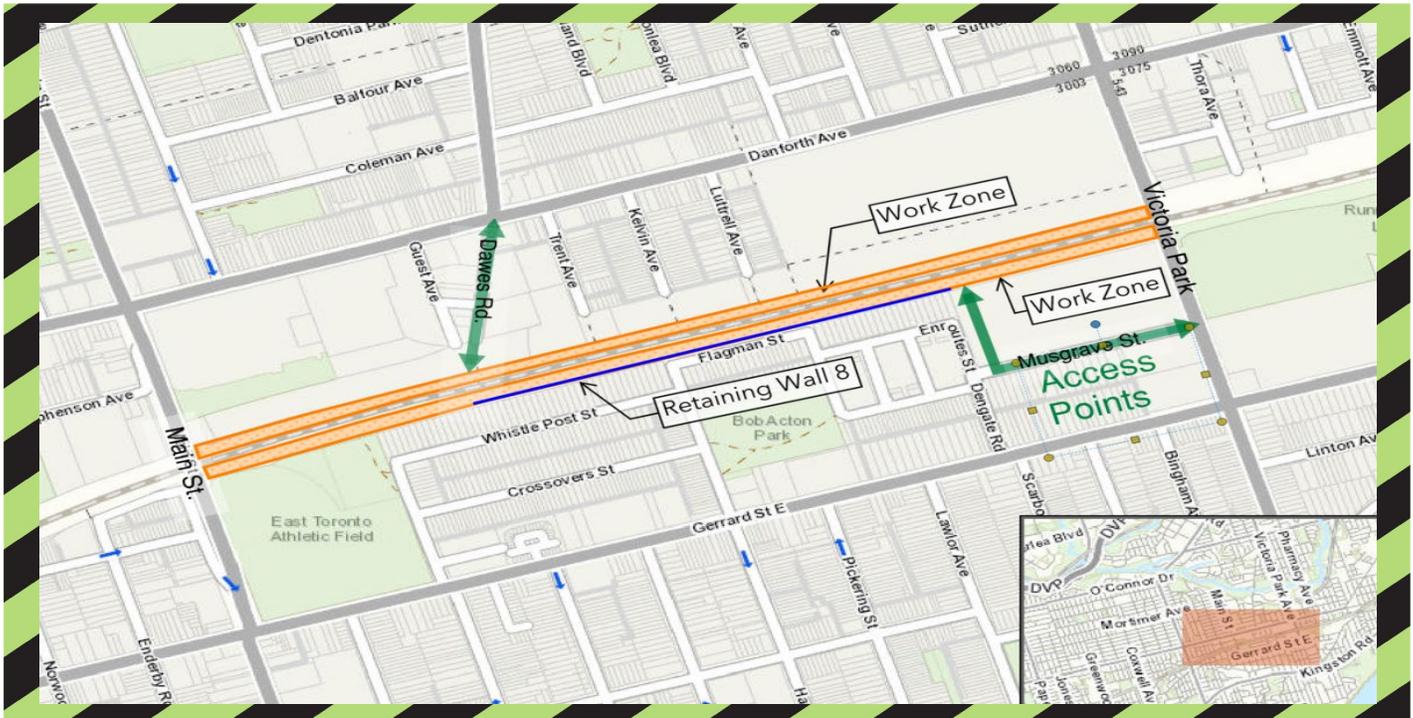

What work is taking place?

Crews are continuing work in the area between Victoria Park and Main Street to perform work along the north and south side of the Lakeshore East rail corridor. This work included installation of sediment control and tree protection fence, tree and vegetation removal followed by earthworks, grading, installation of a retaining wall, electrical raceway, and restoration. Please see below table for details.

Construction Activities	Scheduled Start Date	Expected Duration	Hours of Work	What to Expect
Tree and Vegetation Removal	March 2021 (Complete)	Approx. 1 month	Day Shift	Installation of sediment control and tree protection fence. Tree and vegetation removals to allow for earthworks and grading. Equipment for this work includes: a tree feller, feller buncher, mulcher, dozer, excavator, and dump trucks.
Grading	July 2021 (In progress)	Approx. 10 months	Day & Night Shift	Preparatory work for the retaining wall installation and construction of an access road has been complete. Work will continue final grading following the installation of the retaining wall. Equipment for this work includes: a dozer, dump trucks, and compaction equipment.
Retaining Wall 8	January 2022 (In progress)	Approx. 13 months	Day & Night Shift	Work is continuing on the retaining wall installation which is made up of steel piles drilled into the earth and backfilled with concrete to ground elevation. Pre-cast concrete panels will be placed between the steel piles, above ground level. Equipment for this work includes an excavator, dozer, dump truck, drilling rig, and concrete trucks.

Construction Activities	Scheduled Start Date	Expected Duration	Hours of Work	What to Expect
Electrical Raceway Installation	October 2022	Approx. 3 months	Day & Night Shift	Underground installation of electrical conduit for the future track electrification. Equipment for this work includes: an excavator and packers.
Restoration	April 2023	Approx. 1 month	Day Shift	Installation of topsoil and hydroseed.

* Please note that dates and times are approximate, and work could be rescheduled.
 * Please note that weekend work may be required.

What to Expect

Residents can expect some noise, vibration, dust, and site lighting. Work crews will take reasonable precautions to minimize disturbances to residents, including but not limited to the following:

- No idling of non-essential equipment to reduce the accumulation of construction noise.
- Limited reverse operations and the use of white-noise backup alarms where possible.
- Pointing lights away from residential windows.
- Noise vibration monitoring will be set up to ensure that noise levels are within exposure limits.

HOURS OF WORK

- Day shift work will occur between 7:00 a.m. and 7:00 p.m. five (5) days per week (Monday to Friday).
- Night shift work will occur between 7:00 p.m. and 7:00 a.m. five (5) days per week (Sunday to Thursday).
- Work may be rescheduled due to unforeseen circumstances.

TRAFFIC & PEDESTRIAN DETAILS

- The rail corridor will be accessed through the access roads shown on the map. There will NOT be any construction staging on the access roads.
- Minimal traffic impacts are anticipated.
- Increased construction vehicles and equipment can be expected in the work area.
- Pedestrians will not be impacted at this time.
- TTC will not be impacted at this time.

OTHER INFORMATION

- For the latest information on what's happening in your area please e-mail TorontoEast@Metrolinx.com and ask to subscribe to our weekly e-newsletter.
- Please exercise caution around active construction sites.

PROJECT INFORMATION

- We're making improvements today to bring you even more service in the future. Preparatory early works are underway on the Lakeshore East Rail Corridor Expansion project in Toronto. This project covers the area between Pape Avenue and Kennedy Road. Completing this work will enable the future addition of a fourth track and electrification infrastructure on the Lakeshore East line.
- Electrification is a key part of building a quieter, faster, more efficient network across the region. The new fourth track will improve journey times for all transit trips on the Lakeshore East Corridor, improve reliability and deliver more service within the City of Toronto. For more information on this project and to see all construction notices please visit metrolinx.com/lakeshoreeastrailcorridor.

Thank you for your patience as we work to transform the rail corridor in your area.

Contact Us:

Write to us at: TorontoEast@metrolinx.com
 Find us on Twitter @GOExpansion
 Visit the website: www.metrolinx.com
 Disponible en français
