

York Viva Update

Jack Collins

November 16, 2010

York Viva Project Status






- Funded Rapid Transit* (2010-2015)
- Funded Rapid Transit* (2015-2020)
- Future Rapid Transit*
- - - Spadina Subway Extension
- - - Proposed Light Rail Transit**
- - - Proposed Yonge Subway Extension
- Terminals
- GO Transit Rail Lines



VIVA – 2010 - 2015

Planned In-Service During 2010-15

- York VIVA BRT program – dedicated bus lanes (Rapidways) – will open in operational segments as completed
- Construction started in 2009 on Davis and Enterprise Drive as part of Quick Wins funding
- *2010-15 investment: \$790M (escalated dollars)*

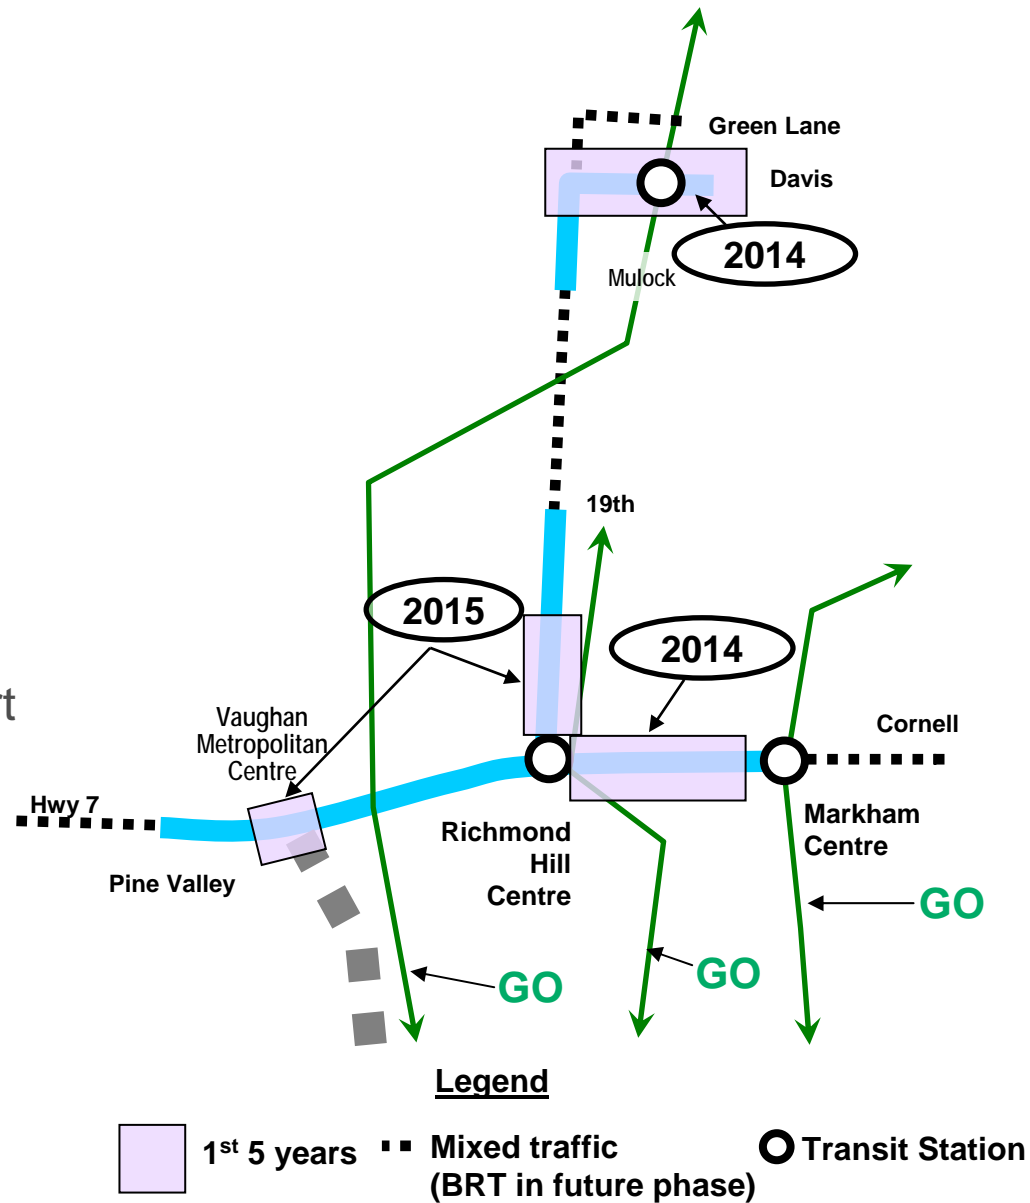


Enterprise Drive – First Segment Complete

- Construction is nearing completion, work included:
 - Grading, paving and platform finishes
 - Installation of new utilities such as sewers electrical and communication
 - Construction of platform foundations
 - Paving
 - Bus shelter / canopy construction
 - Platform finishes
 - Canopy installation
 - Fare collection
 - Communications
 - Traffic signals
 - Landscaping
- Event will be held in November



Davis Drive – Early Works Schedule

- Preparation for construction is underway for Rapidways and the new VIVA stations. Works over the summer and into the fall includes:
 - Demolitions / recycling program
 - Soil testing
 - Retaining wall relocation
 - Keith Bridge work
 - Utility relocation

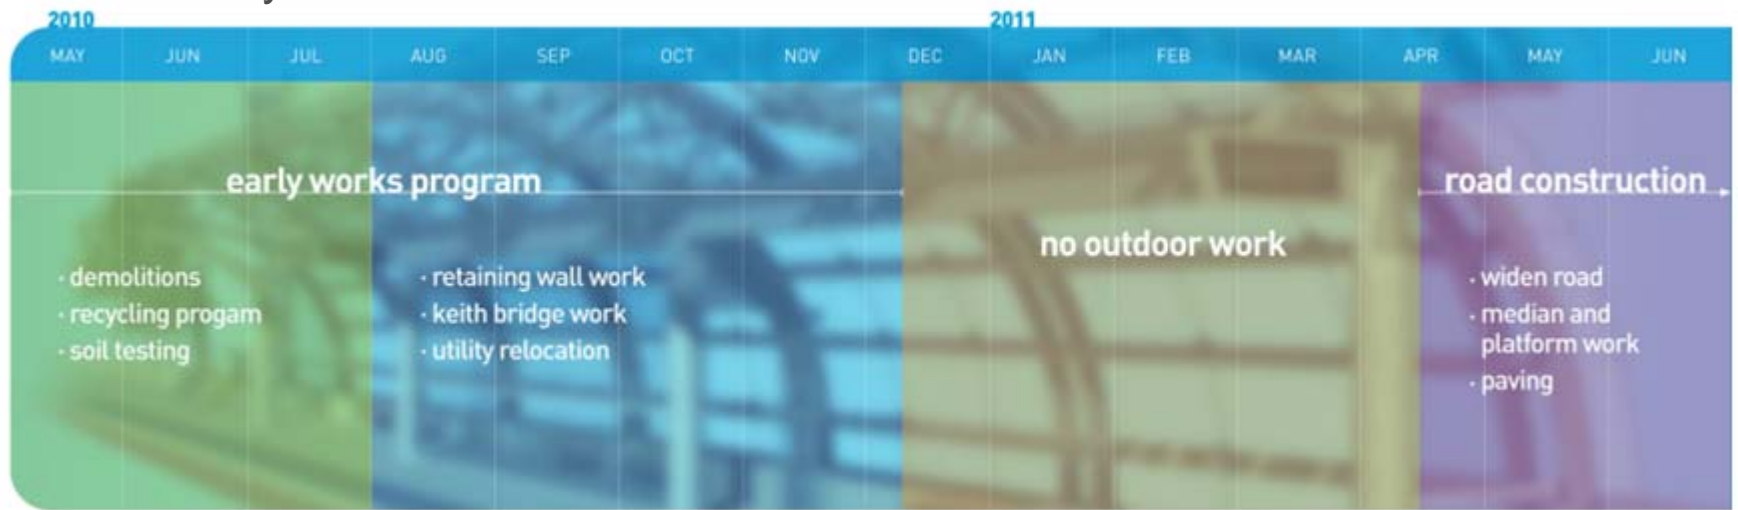


Highway 7 – Yonge to Warden (H3)

- Contract award to Kiewit EllisDon (KED) \$235 million for the design build of the Rapidway and new VIVA stations between Yonge and Markham Centre. Ongoing work includes:
 - Soil testing
 - Utility relocations
 - Final design



VIVA Timelines

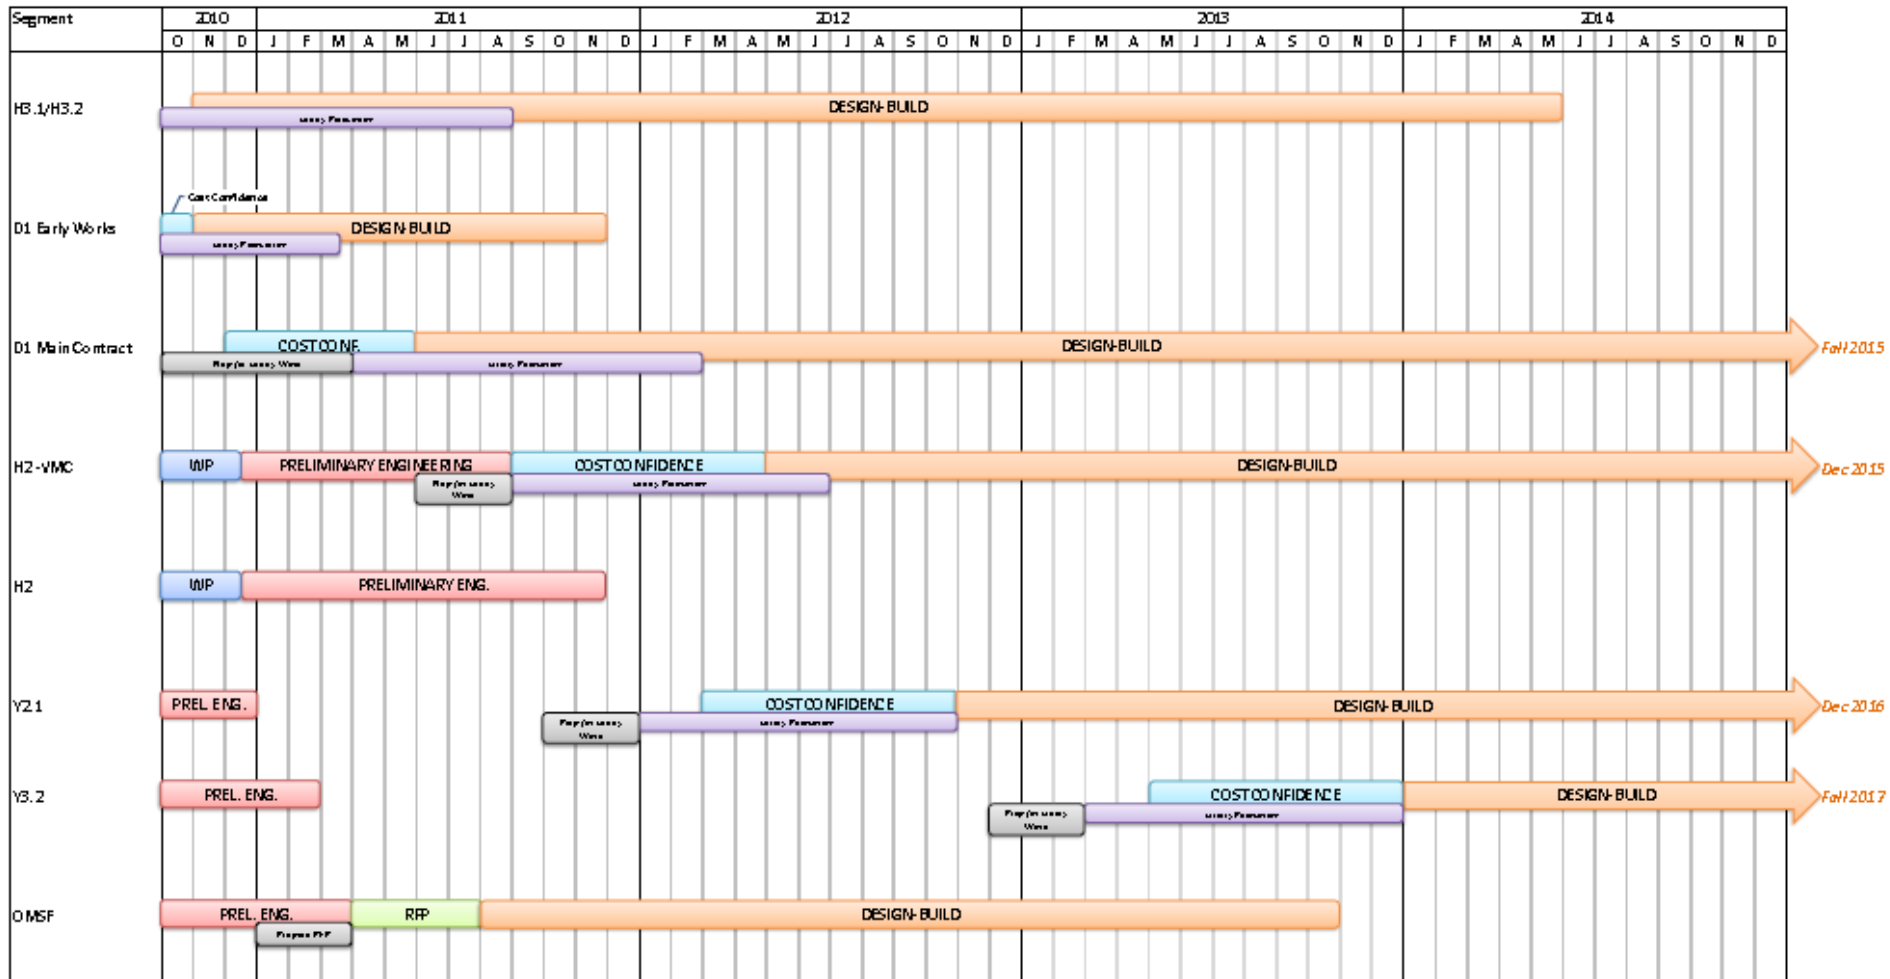

VIVA Budget Trends

The following are the current budget trends for the first three contract segments:

- Enterprise Early Works: On budget
- Real Estate Acquisition: On budget
- Utility Relocations: On budget
- H3 Design Build: \$ 20 million under
- Davis Drive Early Works: \$ 2 million under

* Over \$ 250 million in design and construction contracts awarded to date

Q & A
